

LEGEND

Tree Inventory

Refer to Table 1 of report dated 5 May 2025, revised 17 June 2026 for tree inventory information. All trees greater than 10cm DBH on the subject property and those of all sizes within six metres of the subject property with the potential to be impacted by the proposed development were included in the inventory.

Tree Removals

The removal of 50 trees and one tree polygon will be required to accommodate the proposed site plan, as indicated with RED labels.

Tree Preservation

The preservation of all remaining trees will be possible with the use of appropriate tree protection measures. Trees identified for preservation are indicated with GREEN labels. Tree protection measures will have to be implemented prior to the commencement of the proposed works. Required tree preservation fencing is indicated in MAGENTA. Refer to Tree Protection Plan Notes for preservation details and tree preservation fence detail.

- Tree Label (GREEN), preservation recommended — X
- Tree Label (RED), removal required — X
- Tree Location Estimated by KFCI
- Critical Root Zone (CYAN circle)
- Minimum Tree Protection Zone (MAGENTA circle)
- Minimum Tree Protection Zone of tree identified for removal (shown for select trees)
- Location of Tree Preservation Fencing (thick MAGENTA)
- Location of Air-Spade / Hydro Vacuum Trench (thick CYAN)
- Limit of Significant Woodland per Pinchin

TREE PROTECTION PLAN NOTES

Prior to site disturbance the owner must confirm that no migratory birds are making use of the site for nesting. The owner must ensure that the works are in conformance with the Migratory Bird Convention Act and that no migratory bird nests will be impacted by the proposed work. It is the applicants' responsibility to discuss potential tree injury of trees on shared property lines with their neighbours. Should such trees be injured to the point of instability or death the applicant may be held responsible for removal and such issues would be dealt with in civil court or through negotiation. The applicant would be required to replace such trees to the satisfaction of the City of Burlington.

TREE PROTECTION ZONE: No construction activity including grade changes, surface treatments or excavations of any kind is permitted within the area identified on the Tree Protection Plan or Site Plan as a Tree Protection Zone (TPZ). No root cutting is permitted. No storage of materials or fill is permitted within the TPZ. No movement or storage of vehicles or equipment is permitted within the TPZ. Grade changes are not permitted within established TPZ. The area(s) identified as a TPZ must remain undisturbed at all times.

TREE PROTECTION BARRIERS:

For City-owned Trees:

Tree protection barriers for trees situated on the City road allowance where visibility must be maintained, can be 1.2m (4ft.) high and consist of chain link, or orange plastic web snow fencing on a 2" x 4" wood frame. All supports and bracing used to secure the barrier should be located outside the TPZ. All supports and bracing should minimize damage to roots outside the TPZ. Where some fill or excavate has to be temporarily located near a tree protection barrier, plywood must be used to ensure no material enters the TPZ. If the TPZ needs to be reduced to facilitate construction access, the tree protection barrier must be maintained at a lesser distance and the exposed TPZ protected with plywood and wood chips. This must first be approved by the City of Burlington.

For trees on private property situated on or adjacent to construction sites:

Tree protection barriers must be installed around trees to be protected using plywood clad hoarding or an equivalent approved by the City of Burlington. All supports and bracing to safely secure the barrier should be outside the TPZ. All such supports and bracing should minimize damage to roots outside the TPZ.

General Note:

Prior to the commencement of any site activity the tree protection barriers specified on this plan must be installed and written notice provided to the City of Burlington. Established tree protection zones must not be used as construction access, storage or staging areas. The tree protection barriers must remain in effective condition until all site activities including landscaping are complete. Written notice must be provided to the City of Burlington prior to the removal of the tree protection barriers.

ARBORICULTURAL WORK:

Any roots or branches which extend beyond the TPZ indicated on this plan which require pruning, must be pruned by a qualified Arborist or other tree professional as approved by the City of Burlington. All pruning of tree roots and branches must be in accordance with good arboricultural standards. Roots located outside the TPZ that have received approval from the City of Burlington to be pruned must first be exposed by hand digging or by using a low pressure hydro vac method. This will allow a proper pruning cut and minimize tearing of the roots. The Arborist/tree professional retained to carry out crown or root pruning must contact the City of Burlington no less than 48 hours prior to conducting any specified work.

City of Burlington

TREE PROTECTION ZONE (TPZ)


No equipment or vehicles shall be operated, parked, repaired or refueled within the Tree Protection Zone.

No construction activity, grade changes, surface treatment or excavations of any kind is permitted within the Tree Protection Zone.

No materials or fill may be stored within the Tree Protection Zone.

This tree protection barrier must not be removed prior to the completion of construction without written authorization from the City of Burlington, Urban Forestry Department.

For information, contact:
City of Burlington, Development and Infrastructure Division,
905-335-7642.

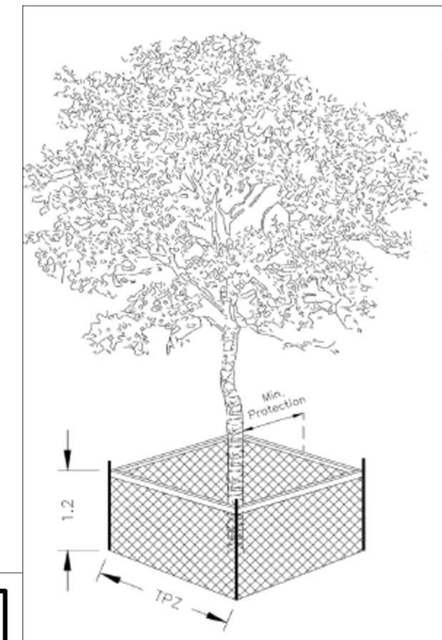

Detail TP-1 – Tree Protection Detail.

Trunk Diameter (DBH) [2]	Minimum Tree Protection Zone (MTPZ) Distances Required [3]	Critical Root Zone (CRZ) Distances Required [3,4]
< 10 cm	1.8 m	1.8 m
11 - 40 cm	2.4 m	4.0 m
41 - 50 cm	3.0 m	5.0 m
51 - 60 cm	3.6 m	6.0 m
61 - 70 cm	4.2 m	7.0 m
71 - 80 cm	4.8 m	8.0 m
81 - 90 cm	5.4 m	9.0 m
91 - 100+ cm	6.0 m	10.0 m

NOTES:

[1] The roots of a tree can extend from the trunk to approximately 2-3 times the distance of the drip line.
[2] Diameter at breast height (DBH) is the measurement of tree trunk taken at 1.4 metres above ground.
[3] Minimum Tree Protection Zone and Critical Root Zone distances are to be measured from the outside edge of the tree base towards the drip line and may be limited by an existing paved surface, provided the existing paved surface remains intact throughout the construction work and is subject to Section 6 of this specification.
[4] Where work is being performed beyond the Minimum Tree Protection Zone but within the Critical Root Zone the works are subject to Section 8 of this specification.

TREE PROTECTION BARRIER

1. The required barrier is a 1.2 metre (4 ft) high orange plastic web snow fencing on 2" x 4" frame. Where orange plastic web snow fencing creates a restriction to sightlines, page wire fencing with reflective tape can be used.
2. Tree protection barriers are to be erected prior to the commencement of any construction or grading activities on the site and are to remain in place throughout the entire duration of the project. The barriers shall be maintained erect and in good repair throughout the duration of construction operations with breaks and unsupported sections repaired immediately. Tree protection may be not be removed prior to the completion of construction without written authorization from the City Arborist.
3. All supports and bracing used to safely secure the barrier should be located outside the MTPZ. All supports and bracing should minimize damage to roots.
4. Where some fill or excavated material must be temporarily located near a MTPZ, a wooden barrier with silt fencing must be used to ensure no material enters the MTPZ.
5. No materials or fill may be stored within the MTPZ.
6. Equipment or vehicles shall not be operated, parked, repaired, or refueled within the MTPZ.
7. No construction activity, grade changes, surface treatment or excavations of any kind is permitted within the MTPZ without written authorization from the City Arborist.
8. A laminated Minimum Tree Protection Zone sign (See Detail TP-3 – Minimum Tree Protection Zone Sign) must be attached to the side of the Tree Protection where it will be visible by persons entering the site. Minimum size must be 10"x14".

No.	Issue/Revisions	Date	By
1	Report Submission	16 Sept. '22	CB
2	Report Revisions	5 May '25	CB
3	Report Revisions	16 Mar. '26	CB
4	Report Revisions	2 June '26	CB
5	Report Revisions	17 June '26	CB

Base Data: MMP Surveyors (topo), Everwest Engineering (civil)

kfci KUNTZ FORESTRY CONSULTING INC.
kuntzforestry.ca
consult@kuntzforestry.ca
289.837.1871
PO Box 1267 Lakeshore W
Oakville, Ontario L6K 0B3

Client
JEC Developments Inc.
5341 John Lucas Dr., 2nd Floor
Burlington, Ontario L7L 6A8

Property
2105 Headon Road
Burlington, Ontario

Tree Inventory and Preservation Plan

Project	P3411	Figure 1
Date	5 May 2025	
Scale	1:200	
